

Government of Rajasthan
RAJASTHAN AGRICULTURAL COMPETITIVENESS PROJECT
II FLOOR, ACADEMIC BLOCK, SIAM CAMPUS, DURGAPURA, JAIPUR-302018
Tel. No. 0141-2554215, 2554218 Fax : 0141-2554214; E-mail: pd@racpmis.com

IFB No.: IN-PMU-RACP-52505-GO-RFB -2018-19/ 7754

Date: 23/8/18

Corrigendum

In reference to IFB No.: IN-PMU-RACP-52505-GO-RFB-2018-19/6398 dated 20.07.2018 for Supply and Installation of Goat Shed in Animal Husbandry Clusters of RACP, following para may be read as:


S. No.	References Clauses	Parameters	Provision in Bidding Document	Amendment in Bidding Document
1	SECTION III. EVALUATION AND QUALIFICATION CRITERIA	2. Post-qualification Requirements (ITB 36.1) (b) Experience and Technical Capacity	The Bidder shall furnish documentary evidence to demonstrate that it meets the following experience requirement (s): The bidder must have supplied and installed the pre-fabricated Sheds for animal/office/factory or any other similar nature of goods/works in last five years (From Year 2013-14 to 2017-18) with minimum total quantity 300 Nos.	The Bidder shall furnish documentary evidence to demonstrate that it meets the following experience requirement (s): The bidder must have supplied and installed the pre-fabricated Sheds for animal/office/factory or any other similar nature of goods/works in last five years (From Year 2013-14 to 2017-18) with minimum total quantity 300 Nos or 30,000 sq. ft.
2	SECTION VII – SCHEDULE OF REQUIREMENTS	2. Technical Specifications	Addition to Technical Specification	Inclusion of pre Cast method for the construction of Goat shed as per specifications in annexure 1.
3	SECTION VII – SCHEDULE OF REQUIREMENTS	3. Drawings	Addition to Drawings	Inclusion of pre Cast method for the construction of Goat shed as per drawings in annexure 2

The bid submission date is extended up to 10th September, 2018 at 2.00 PM. The bid will be opened on same date at 2.30 PM.

Other terms and conditions of bidding document will remain unchanged.

Encl.: Annexure 1 & 2.

Bidding Documents and corrigendum may be viewed and downloaded from website <http://www.agriculture.rajasthan.gov.in/content/agriculture/en/RACP-dep.html>.


 (Dr. Om Prakash)
 Project Director

Annexure - 1

Technical Specification for Pre Cast Method


Goat Shed

1. Levelling of the ground to the desired height so that water logging doesn't happen inside the shed. But upto a maximum height of 1'0"
2. Placing Precast Floor cum Foundations over the levelled ground of 75 mm thick 8 mm tor @ 250 c/c with hooks.
3. Precast Walls of 1000 mm height fixed over the foundation floor with tongue and groove joint. Walls to have bolts to receive the baseplate of the steel structure.
4. Steel pipe columns fixed over these walls with baseplates which do the work of joining the top of walls as well.
5. Steel pipe / angle purlins
6. Hot Rolled dipped sheet of blue colour fixed over the purlins to be fixed on the purlins
7. Gate made of pipe / angles with chain link fencing in between 1000 x 2100
8. Fixing Chain link fencing all around to full height
9. White wash on all Walls
10. White synthetic enamel on all steel members and chain link fencing.

Specifications


1. Precast RCC members to be made with M25 concrete and having steel of 8 mm tor steel @ 250 mm c/c . With proper hooks for lifting and fixing
2. Steel Columns beam and purlins to be MS pipe 48 x 48 x 2.1 mm or Angle 50 x 50 x 6
3. Chain link fencing of 75 x 75 size made of 2 mm wire
4. Hot Rolled dipped sheet of blue colour on roof 26 gauge.

GOAT SHED

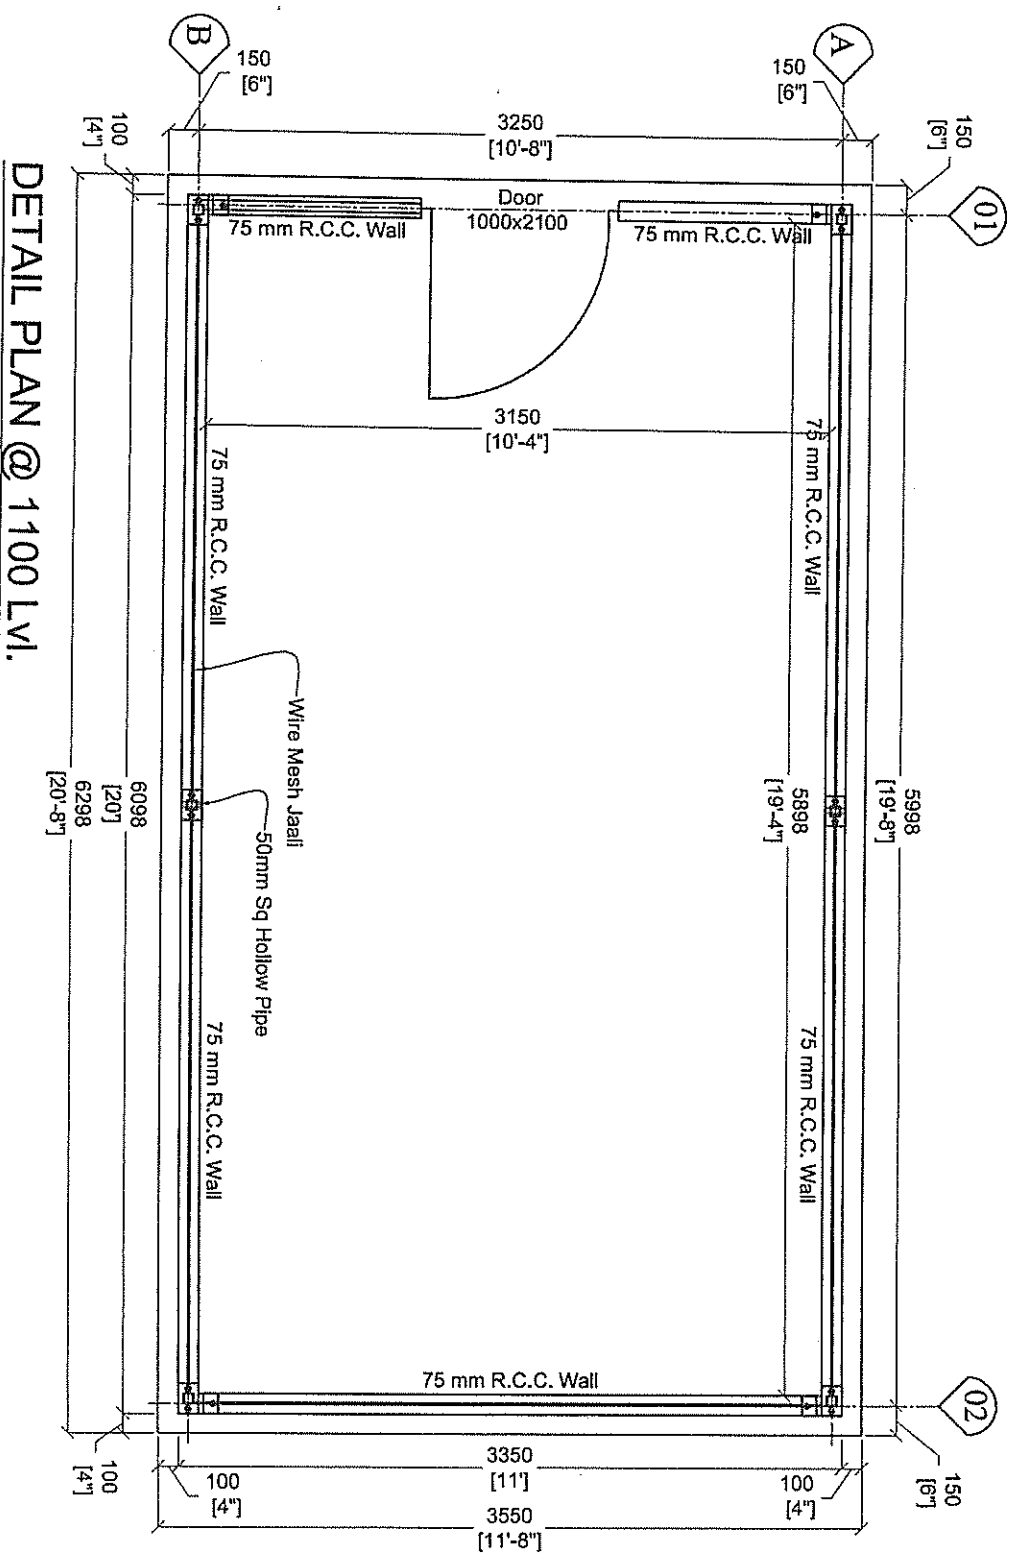


DETAIL PLAN @ 1100 LVL.

GOAT SHED

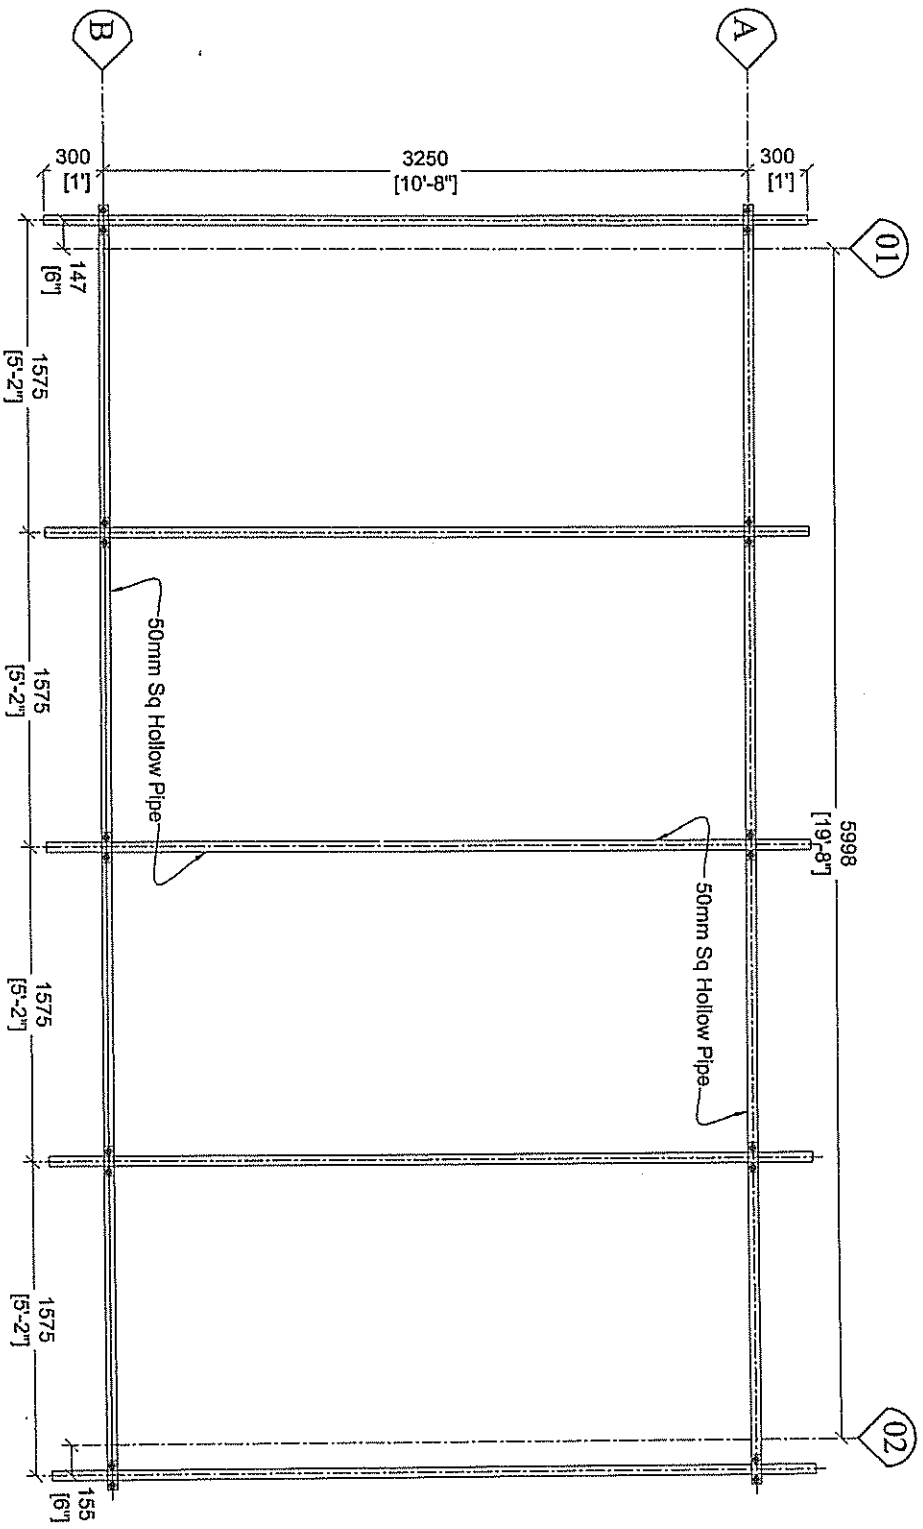

ROOF PLAN

GOAT SHED

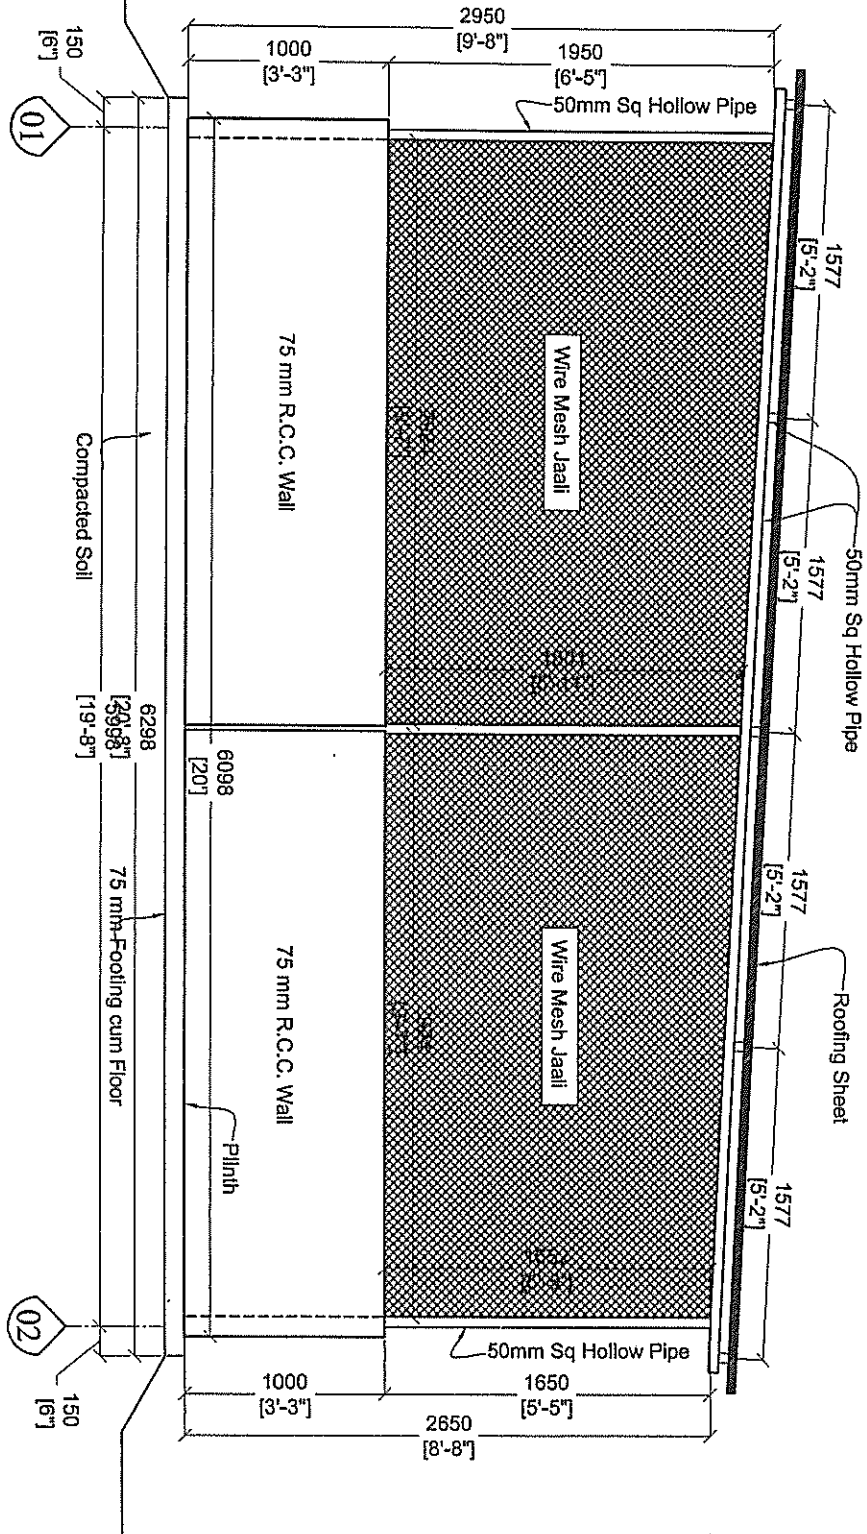


SIDE ELEVATION

01


02

GOAT SHED

REAR ELEVATION

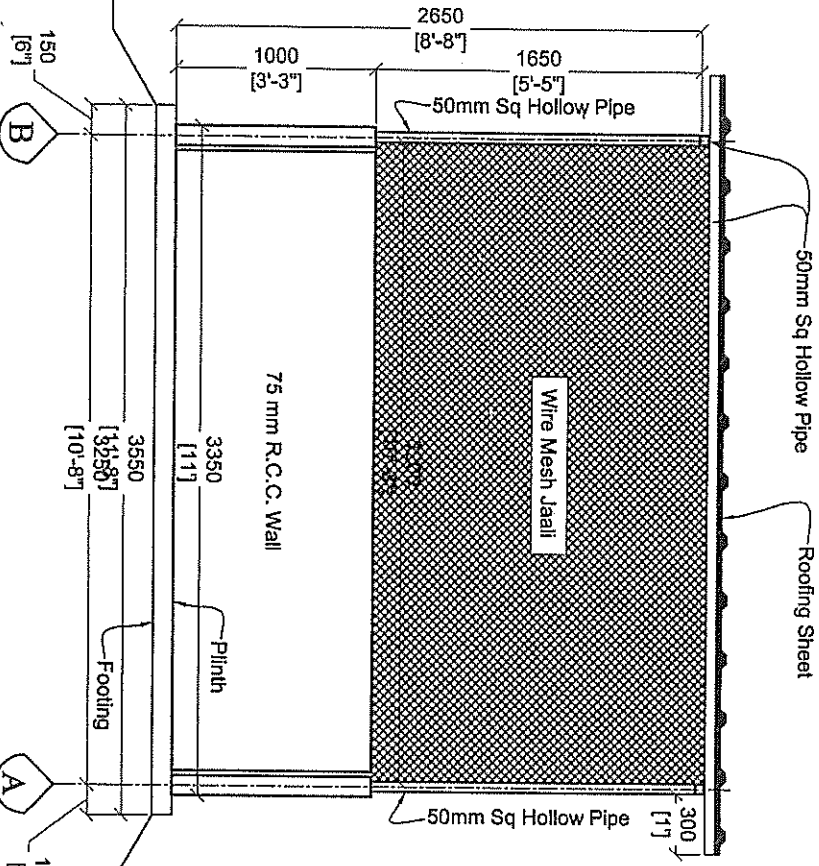



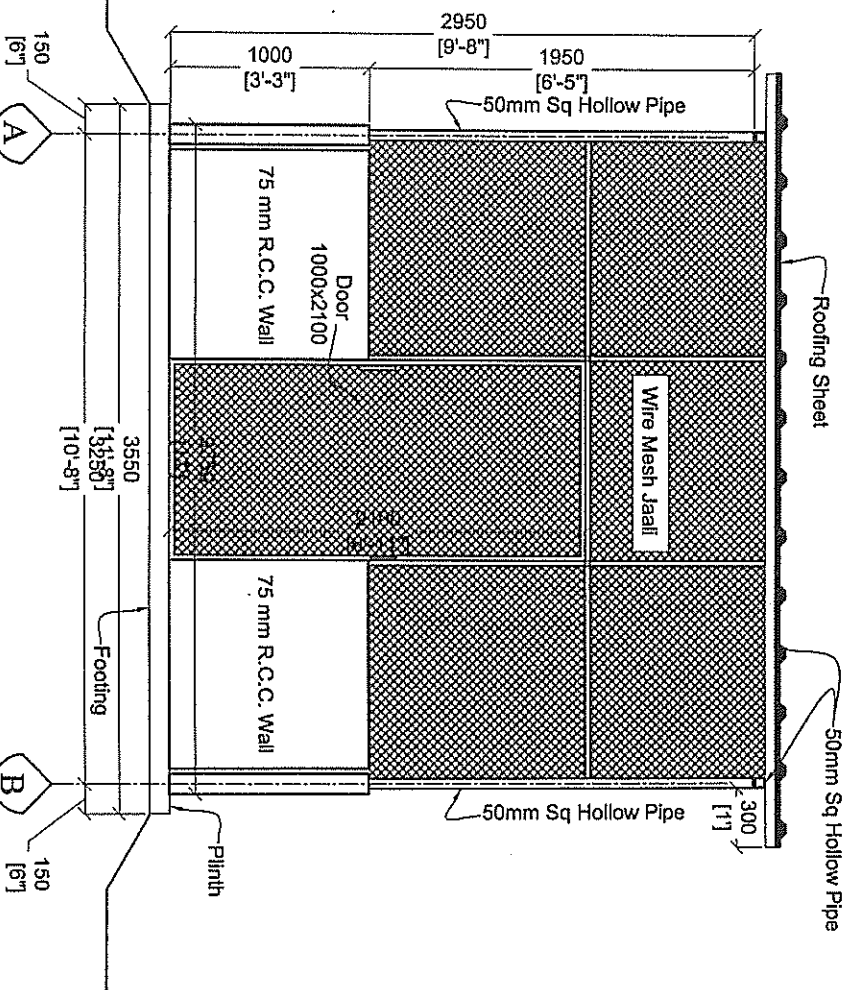



FRONT ELEVATION



Pre Bid Meeting for Supply and Installation of Goat Shed in Animal Husbandry Clusters of RACP

Date - 03.08.2018 at 11.30 AM

PMU, RACP, Jaipur

Sr. No.	Name	Designation/Organization	E-mail ID (IN CAPITAL LETTERS)	Mobile No.	Signature
1.	MAHENDRA INTERNATIONAL	Project Manager	ISHANTINTERNATIONAL1947@YAHOO.CO.IN	8122638869	
2.	DEEPAK SOJANI	Katha Group Builder	rmd	9829036951	
3.	DIP SINGH	PCL (B)			
4.	Anand Singh	PCW/S		94142-5745	
5.	Hansraj Singh	Asst Manager Account			
6.	Vijay Kumar Khanna	LI			
7.					
8.					
9.					
10.					
